


**NORTH WESTERN RAILWAY  
SYSTEM MAP  
SANCTIONED NL/GC/DL WORKS ( IN PROGRESS )**

**LIST OF SANCTIONED WORKS OVER NWR**

Sr. No.	NAME OF WORK	SALIENT FEATURES			PHYSICAL PROGRESS & TDC
		YEAR OF SANCTION	COST IN Cr.	LENGTH IN KM	
<b>A. NEW LINE</b>					
1	DAUSA - GANGAPUR CITY NEW LINE Dausa-Deedwana, CRS done on 17 & 18.08.2017. GGC - Piplai, CRS done on 09.03.2021. Piplai - Lalsot, CRS done on 03.03.2023.	1996-97	950.00	94.65	Lalsot-Deedwana = 72% (TDC: Sep-23)
2	RATLAM - DUNGARPUR via BANSWARA Bankability study report sent to RB in Feb-2020 with ROR (+)2.73%.	2011-12	4500.00	188.85	Cost sharing with Govt. of Rajasthan Execution of work kept in abeyance by RB. Letter written to RB on 10.04.23 for revival of project.
3	AJMER(NASIRABAD) - KOTA (JALINDRI)	2013-14	822.00	145.00	Execution of work kept in abeyance by RB on 24.09.2019.
4	AJMER (AII)- SAWAI MADHOPUR (SWM) via TONK Bankability study report sent to RB in July-2021 with ROR (-)7.85%.	2015-16	2215.27	165.00	Cost sharing with Govt. of Rajasthan. Execution of work kept in abeyance by RB.
5	TARANGA HILL- ABU ROAD (ABR) VIA AMBAJI	2017-18	2798.16	116.65	Land acquisition is in progress. (TDC: 31.12.26)
6	DEDICATED TEST TRACK FOR RDSO (i) GUDHA - THATHANA MITHRI NL (PHASE-I) Twisted track (4.5 Km) commissioned on 30.12.20. (ii) RDSO DEDICATED TEST TRACK (PHASE-II)	2018-19	353.48	22.80	60% (TDC: 30.12.23)
7	NATHDWARA - NATHDWARA TOWN NEW LINE	2018-19	166.33	9.60	Land acquisition is in progress. (TDC: 30.06.25)
8	NIMACH-BADI SADRI NEW LINE	2017-18	495.18	48.35	Land acquisition is in progress. (TDC: 31.03.26)
<b>B. GAUGE CONVERSION</b>					
9	DEVGARH-NATHDWARA (82.54 KM) GC PART OF MARWAR - MAVLI	2017-18	968.92	82.54	DPR sanctioned by RB on 24.01.2023. Land acquisition is in progress.
<b>C. DOUBLING</b>					
10	PHULERA - DEGANA DOUBLING (i) DNA-BOW : COMMISSIONED ON 27.10.2021. (ii) BOW-KMNC : COMMISSIONED ON 15.03.2022.	2015-16	701.81	108.00	(i) KMNC-NAC = 72% (TDC=Oct-23) (ii) NAC-GVMR= 64% (TDC= Dec-23) (iii) GVMR-FL = 64% (TDC=July-23)
11	BHATINDA - DEGANA DOUBLING	2020-21	4800.00	480.00	Bhatinda-Degana Doubling (480 Km) work is kept in abeyance by RB vide letter dt. 26.10.2021.
12	SAWAI MADHOPUR -BYEPASS LINE	2020-21	239.54	13.54	DPR sanctioned by RB on 09.12.22. Land acquisition is in progress. (TDC= 31.12.24).
13	REWARI-KATHUWAS DOUBLING	2022-23	352.41	27.73	DPR sanctioned by RB on 03.02.23. Tender work in process.
14	CHURU-RATANGARH DOUBLING	2022-23	422.60	42.81	DPR sanctioned by RB on 03.02.23. Tender work in process.
15	BHIWANI - DHOB BAHALI DOUBLING	2022-23	471.06	42.30	DPR sanctioned by RB on 27.02.23. Tender work in process.
16	MANHERU - BHIWANI KHERA DOUBLING	2022-23	413.09	31.50	DPR sanctioned by RB on 10.04.23. Tender work in process.
17	KATHUWAS - NARNAUL DOUBLING	2022-23	313.31	24.12	DPR sanctioned by RB on 10.04.23. Tender work in process.
<b>D. CAPITAL INVESTMENT (JV awaited with GOR)</b>					
18	KISHANGARH - PARBATSAR NEW LINE	2016-17	900.00	45.0	MoU with Rajasthan Government is yet to be signed for creation of SPV.
19	JAISALMER - BHABAR NEW LINE	2016-17	5000.00	339.0	MoU with Rajasthan Government is yet to be signed for creation of SPV.

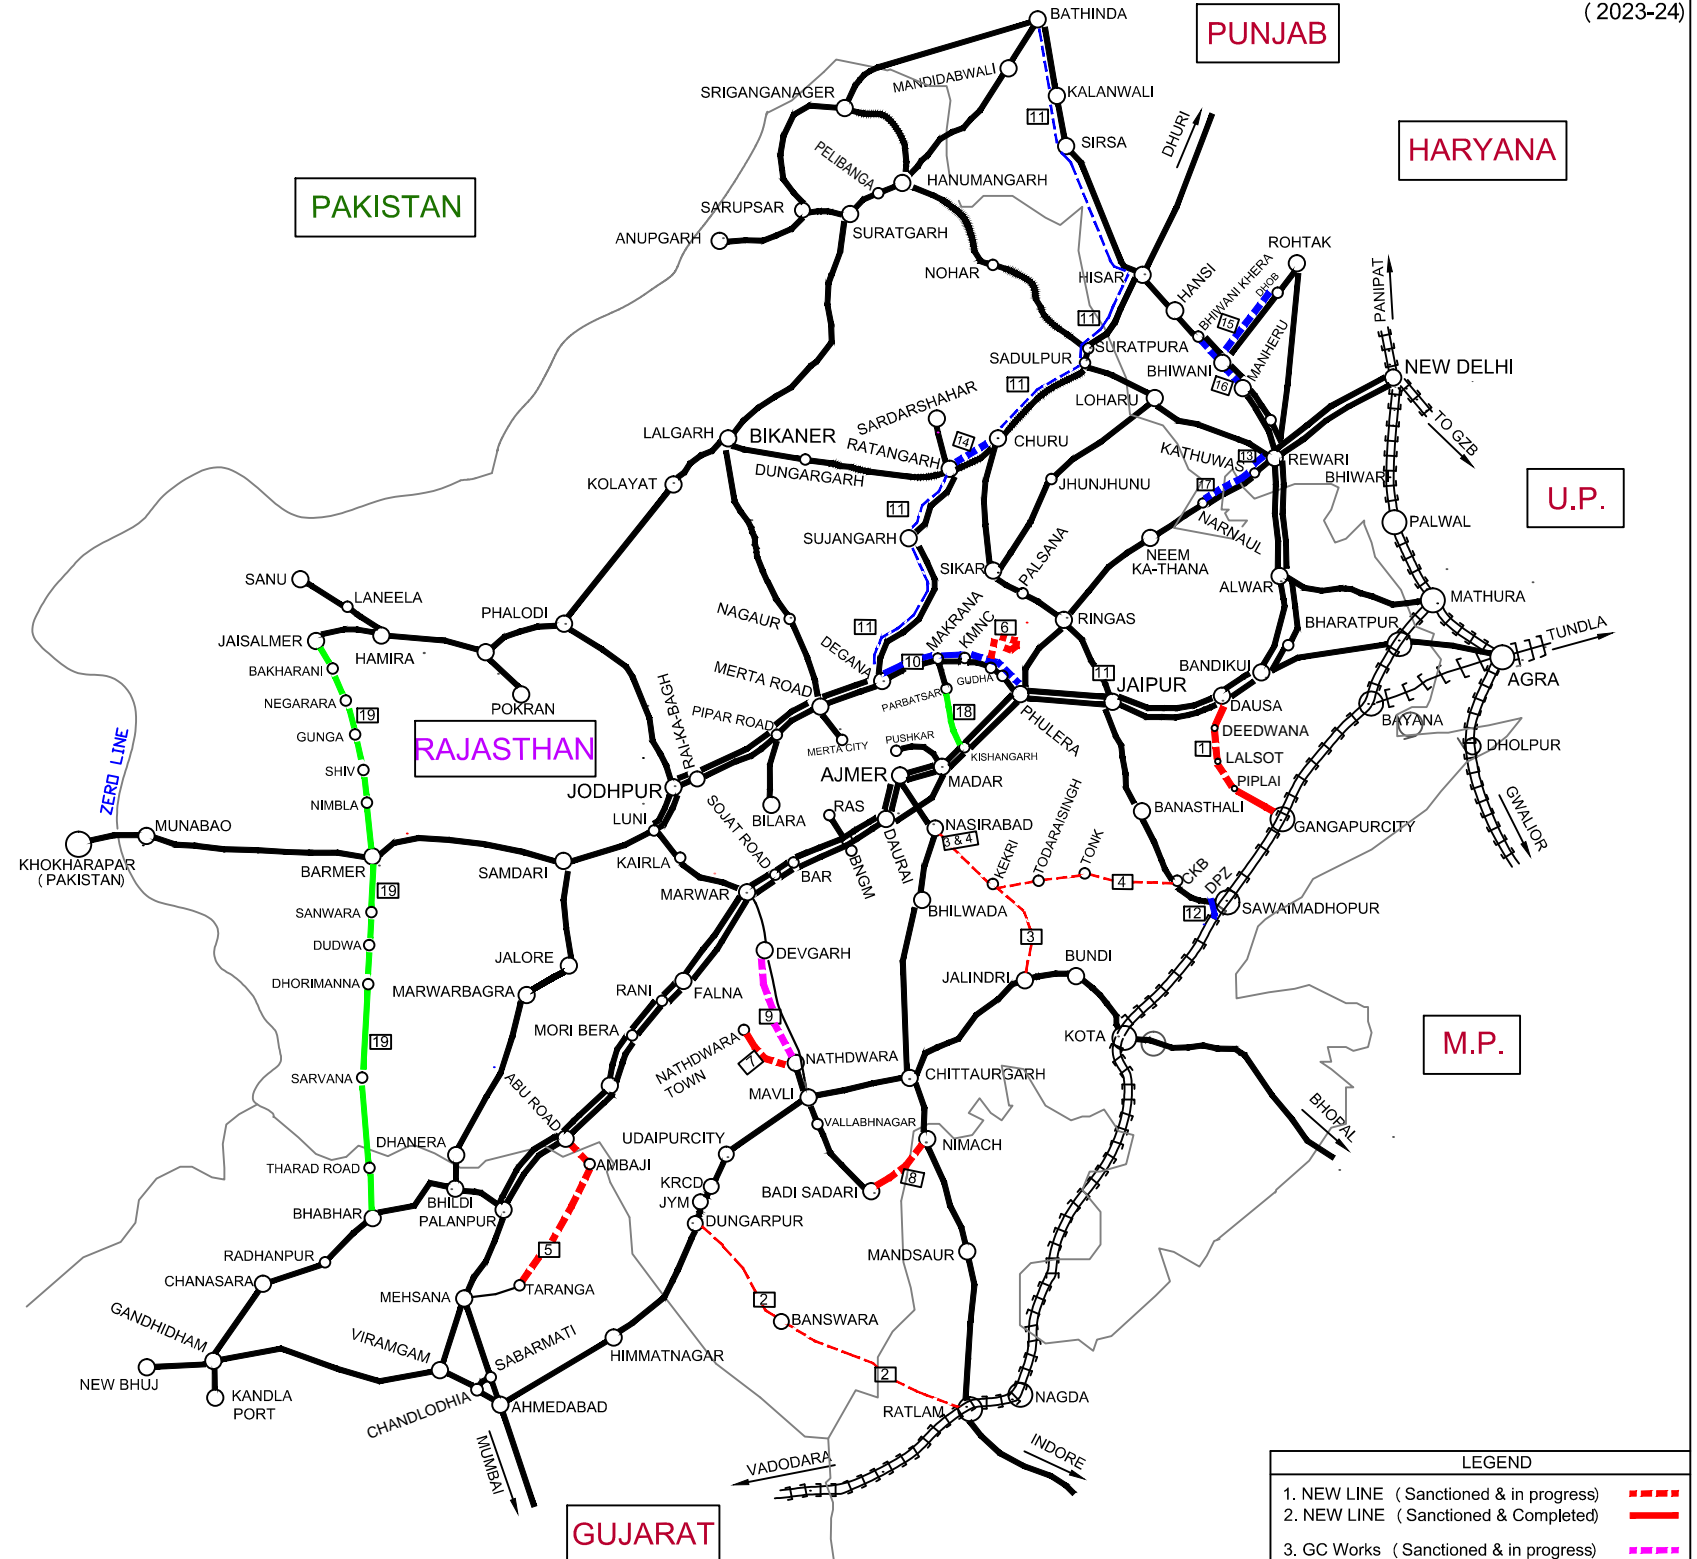

**LEGEND**

1. NEW LINE ( Sanctioned & in progress )	----
2. NEW LINE ( Sanctioned & Completed )	————
3. GC Works ( Sanctioned & in progress )	----
4. GC Works ( Sanctioned & Completed )	————
5. DOUBLING ( Sanctioned & in progress )	----
6. DOUBLING ( Sanctioned & Completed )	————
7. Kept in abeyance works :-	
NL Works	----
GC Works	----
DL Works	----
8. CAPITAL INVESTMENT ( Sanctioned )	————
