PRODUCED BY AN AUTODESK EDUCATIONAL PRODUCT

# NORTH WESTERN RAILWAY

AS ON 24-02-2020

## LIST OF SANCTIONED WORKS OVER NWR

| Sr. No. | NAME OF WORK | SALIENT FEATURES: YEAR OF SANCTION | COST IN CR | LENGTH IN KMS | PHYSICAL PROGRESS & TDC |
|---|---|---|---|---|---|
| **1.0 NEW LINE** | | | | | |
| 1.1 | DAUSA (DO) - GANGAPUR CITY (GGC) | 1996-97 | 780.98 | 92.67 | 83% GGC-Khurda TDC30.09.2021 Khurda - Deedwana TDC28.02.2021. |
| | DO-Deedwana CRS done on 17.08.17 &18.08.17. | | | | |
| 1.2 | RATLAM(RTM)-DUNGARPUR(DNRP) Via-BANSWARA(BNSW) | 2011-12 | 2417.24 | 166.85 | 6.25% , Execution of work kept in abeyance by RB. |
| | Bankability study is being done by Operating Department. | | | | |
| 1.3 | THAIYAT HAMIRA(THM)-SANU | 2013-14 | 262.46 | 58.50 | 100%. |
| | Commissioned on 31-12-2019 for Goods Trains. | | | | |
| 1.4 | AJMER(AII)-KOTA NASIRABAD(NSD)-JALINDRI | 2013-14 | 822.00 | 145.00 | Execution of work kept in abeyance by RB. |
| | CCEA sanction is yet to be obtained by Rly Bd. | | | | |
| 1.5 | PUSHKAR (POHT) - MERTA (MTD) | 2013-14 | 323.00 | 59.00 | Execution of work kept in abeyance by RB. |
| | CCEA sanction is yet to be obtained by Rly Bd. | | | | |
| 1.6 | AJMER (AII)- SAWAI MADHOPUR (SWM) VIA TONK | 2015-16 | 873.71 | 165.00 | Execution of work kept in abeyance by RB. |
| | (i)State Govt. refuse to share cost. (ii)Bankability study is being done by operating department. | | | | |
| 1.7 | TARANGA HILL - ABU ROAD (ABR) VIA AMBAJI | 2017-18 | 1695.72 | 89.38 | FLS in progress. |
| | (i)Sanctioned in FS 2017-18 (ii)DPR duly appr. by GM submitted to Rly. Bd. | | | | |
| 1.8 | GUDHA - THATHANA MITHRI NEW LINE (DEDICATED TEST TRACK) | 2018-19 | 353.48 | 55.00 | Work in progress. |
| **2.0 GAUGE CONVERSION WORKS** | | | | | |
| 2.1 | MAVLI Jn (MVJ) - BARI SADRI (BI) | 2013-14 | 295.02 | 82.01 | 89% Dec, 20 |
| | (i)Section closed on 01.11.2016 for GC works. (ii)Contract terminated and new contracts awarded. | | | | |
| 2.2 | JAIPUR(JP)-SIKAR(SIKR) & SIKAR(SIKR)-CHURU(CUR) | 2008-09 | 658.07 | 320.04 | 100% |
| | (i) Sikar - Loharu (122.13 Km) Commissioned on 01.08.2015. (ii)Sikar - Fatehpur Shekhawati (47.06 Km) Commissioned on 29.06.17. (iii) Fatehpur Shekhawati - Churu (43.40 Km) Inauguration 09.12.17 (iv)Sikar-Palsana (27 Km) Commissioned on 27.01.2019. (v)Palsana-RINGAS(23 Km) Commissioned on 27.01.2019. (vi) JP - RGS (89 Km) Commissioned on 21.10.2019. | | | | |
| 2.3 | HIMMATNAGAR (HMT) - UDAIPUR (UDZ) | 2008-09 | 629.74 | 208.08 | 99% 1.DNRP-RGQ May,20 2.DNRP-JYM Feb,21 3.JYM-KRDD Nov,21. |
| | Work is in progress. (i)RGQ-HMT,CRS DONE on 29.05.19. (ii) UDZ-KRDD,CRS DONE ON 15.01.2020. | | | | |
| 2.4 | MARWAR (MJ) - MAVLI (MVJ) (NATHDWARA) | 2017-18 | 1597.12 | 152.00 | Execution of work kept in abeyance by RB. |
| | (i).Sanctioned in FS 2017-18 (ii)DPR,duly appd. by GM ,submitted to Rly. Bd. | | | | |
| **3.0 DOUBLING** | | | | | |
| 3.1 | AJMER (AII) - BANGURGRAM (BNGM) | 2011-12 | 218.39 | 48.43 | 99%, 1.AII-DAURAI Dec,20. |
| | (i) BNGM-MLJ Commissioned on 27.09.2018. (ii)DOZ-MLJ Commissioned on 28.11.2019. | | | | |
| 3.2 | GURIYA (GRI)-MARWAR Jn (MJ) | 2011-12 | 208.22 | 43.50 | 100% |
| | (i) MJ-SOD commissioned in Feb 2017,(ii) SOD-CNL Commissioned in April 17,(iii) CNL-GRI Commissioned on 30.12.17. | | | | |
| 3.3 | BANGURGRAM (BNGM) - GURIYA (GRI) | 2012-13 | 348.55 | 47.00 | 99% , 1.BNGM-SENDRA CRS insp. sched on 28.02.20. 2.SENDRA-HP Feb,21. |
| | (i) Composite contract, amounting Rs174.00cr, awarded on 11.11.2016. (ii)HP-GRI commissioned on 14.09.2018. | | | | |
| 3.4 | RANI(RN)-MARWAR Jn(MJ). | 2012-13 | 335.53 | 51.82 | 100% |
| | (i) Composite contract, amounting Rs182 cr, awarded on 30.12.2015. (ii)BWA-MJ,commissioned on 24.04.18. (iii) RN-BWA, Commissioned on 09.01.2019. | | | | |
| 3.5 | ALWAR (AWR)- BANDIKUI (BKI) | 2013-14 | 281.03 | 60.37 | 99% DGW-BKI, CRS insp. scheduled on 28/29.02.20 |
| | AWR-DGW Commissioned on 31.01.2019. | | | | |
| 3.6 | PHULERA (FL) - DEGANA (DNA) | 2015-16 | 611.53 | 108.00 | 15% |
| | (i) DNA-MKN (ii) MKN-NAC (iii) NAC-FL | | | | DNA-MKN Jan.21 MKN-NAC June.21 NAC-FL Apr.22 |
| 3.7 | DEGANA (DNA)-RAIKA BAGH (RKB) | 2018-19 | 808.85 | 145.00 | 11% |
| | (i).DNA-MTD (ii).MTD-PPR (iii).PPR-RKB | | | | DNA-MTD Mar.21 MTD-PPR Dec.21 PPR-RKB Sept.22 |
| 3.8 | JAIPUR - SAWAIMADHOPUR DOUBLING | 2019-20 | | 131.27 | |
| **4.0 DOUBLING (RVNL)** | | | | | |
| 4.1 | ABU ROAD (ABR) - SAROTRA ROAD (SZA) | 2010-11 | 131.41 | 23.12 | 100% |
| | (i) Abumod - Mavli ,commissioned on 24.01.2020. (ii).MAA-SZA Commissioned on 02.02.19. | | | | |
| 4.2 | SWROOPGANJ (SRPJ)- ABU ROAD (ABR) | 2010-11 | 134.55 | 25.36 | 100% |
| | (i)SRPJ-SMN commissioned on 31.05.17. (ii) ABR-SMN commissioned on 24.01.2020. | | | | |
| 4.3 | SAROTRA ROAD (SZA) - KARJODA (KRJD) | 2010-11 | 194.13 | 23.59 | 99% March,20. |
| | Work complete except Jethi - Karjoda section . (i).SZA-JTY Commissioned on 02.02.19. | | | | |
| 4.4 | RANI (RN) - KESHAVGANJ (KVJ) | 2011-12 | 277.61 | 59.50 | 100% |
| | Work completed and Commissioned on 29.03.18. | | | | |
| 4.5 | REWARI (RE) - MANIHERU (MHU) | 2011-12 | 373.61 | 69.02 | 100%, |
| | (i) Rewari(RE)-Kosli(KSI) Commissioned on 05.03.17, (ii)Kosli - Jhasi Commissioned on 11.02.18 & (iii)Work is in progress in JRL-MHU. | | | | |
| 4.6 | KARJODA (KRJD) - PALANPUR (PNU) | 2011-12 | 26.00 | 5.40 | 100% |
| | Work Completed. CRS Inspection done on 18.08.18. | | | | |

## SYSTEM MAP

### SANCTIONED WORKS (IN PROGRESS)

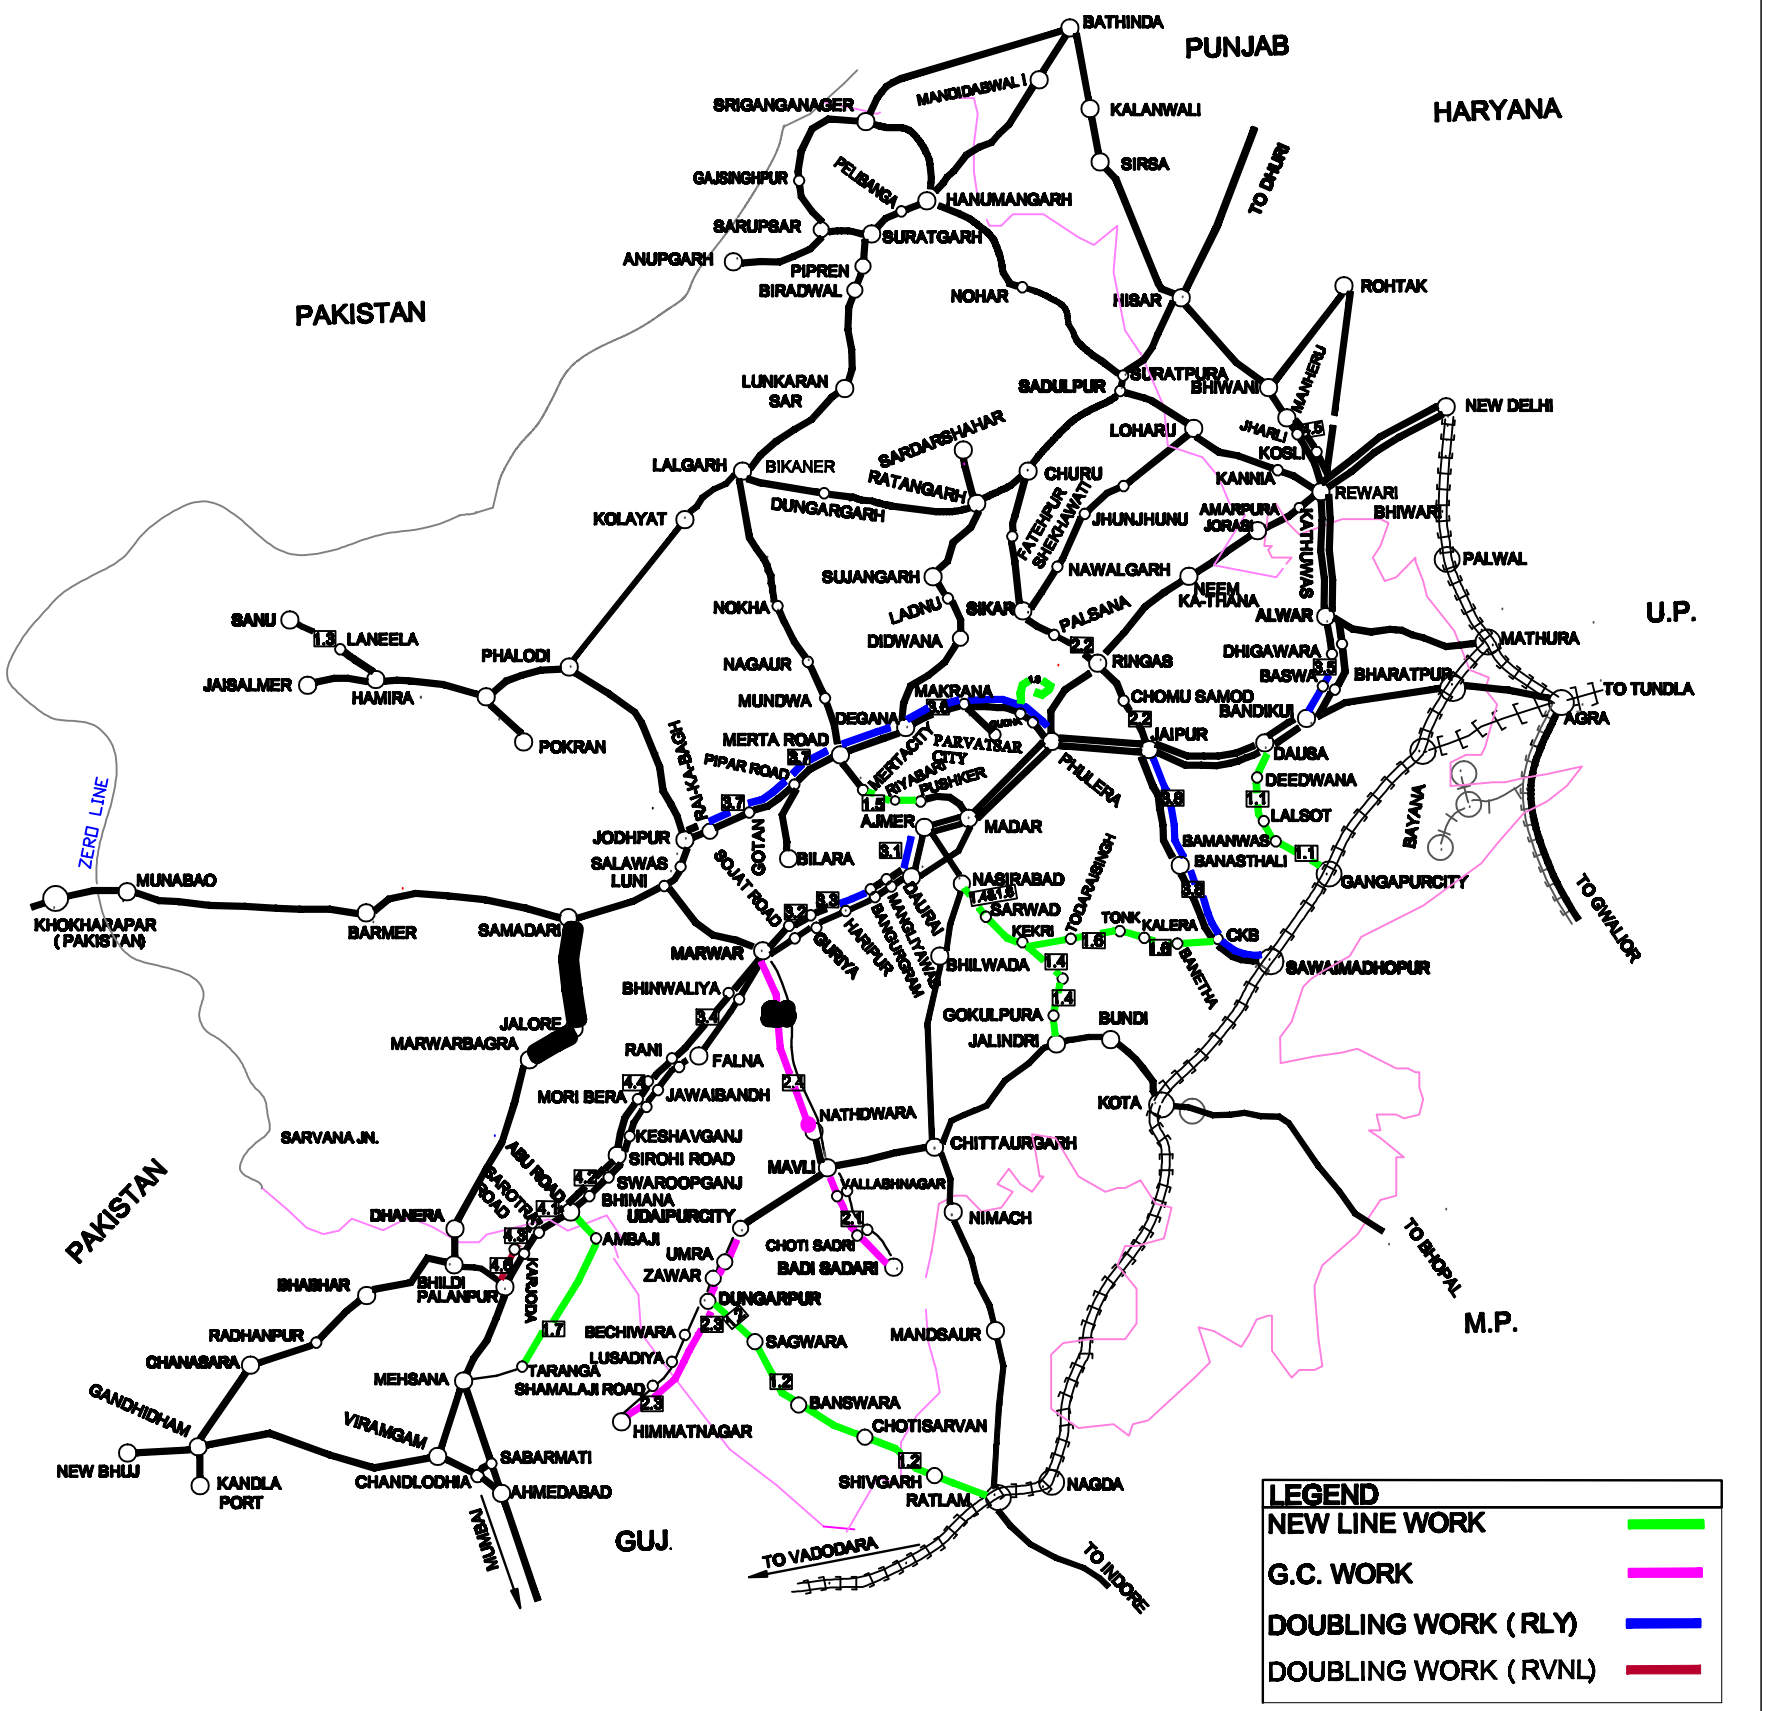


PRODUCED BY AN AUTODESK EDUCATIONAL PRODUCT

PRODUCED BY AN AUTODESK EDUCATIONAL PRODUCT

PRODUCED BY AN AUTODESK EDUCATIONAL PRODUCT
